

**report to  
Board of Trustees****Construction Projects Status Report**

Date	September 23, 2025
Meeting Type	Regular Meeting, Public Agenda
To	Board of Trustees
From	Joanne Pitman Chief Superintendent of Schools
Purpose	Information
Originator	Dany Breton, Superintendent, Facilities and Environmental Services
Governance Policy Reference	Operational Expectations OE-7: Communication With and Support for the Board OE-9: Facilities
Resource Person(s)	Trevor Fenton, Director, Facility Projects David Jaimes, Manager, Capital Construction

**1 | Recommendation**

---

This report is being provided for information to the Board of Trustees. No decision is required at this time.

**2 | Issue**

---

The Chief Superintendent is required to provide the Board of Trustees with an update regarding the status of major capital projects including new schools, modernizations, additions and Modular Classroom Program (MCP) projects currently under development or construction.



### 3 | Background

---

The Calgary Board of Education (CBE) has received construction approval for four new schools, design approval for ten new schools, one modernization, and one replacement school, and planning approval for one new school.

On March 4, 2022, the Government of Alberta (GoA) announced “Design and Construction” approval of a middle school in the community Evanston. On December 14, 2022, Alberta Infrastructure (AI) advised that the school will be delivered via a design-build delivery method. The design-build contract was awarded in November 2023 and construction commenced on April 25, 2024. On August 29, 2025, the CBE announced that the name of the new middle school will be Evanston Heights School.

On March 1, 2023, the GoA announced the approval of “Design and Construction” funding for the modernization of John G. Diefenbaker High School. A pre-design report outlining findings from stakeholder engagement and consultant site reviews was issued in December 2023. The report identified a significant funding gap between the approved budget and the required scope of work. On April 16, 2024, Alberta Education and Childcare (AE&C) granted approval to extend project timelines to allow CBE to conduct additional planning activities to further evaluate the project scope prior to proceeding with design. The results of the CBE planning activities were shared with AE&C and on July 16, 2025, AE&C informed CBE of the approval to change the project’s scope of work from modernization to full replacement. The replacement school will have an opening capacity of 1,910 students, representing a capacity increase of 505 students compared to the current building. Moreover, the school will be designed to be able to accommodate an additional 195 students through the installation of modular classrooms in the future, if required. The project will be managed by AI and is approved for design only, with further approvals required to obtain construction funding.

On March 1, 2024, the GoA announced approval of “Design and Construction” funding for a new elementary school in the community of Evanston and “Design” funding for a new elementary school in the community of Redstone and a new high school in the community of Cornerstone. On August 8, 2024, the GoA approved a capacity increase of the Cornerstone high school from 1,800 to 2,410 students and on December 3, 2024, approval was received for a capacity increase of Redstone elementary from 600 to 890 students. AI commenced pre-design work on August 6, 2024, for Evanston elementary, October 7, 2024, for Redstone elementary and December 13, 2024, for Cornerstone high school. On February 15, 2025, the GoA announced construction approval for both Redstone elementary and Cornerstone high school. All three schools will be delivered as Public-Private Partnership (P3) projects.

On March 1, 2024, the GoA announced approval of “Design” funding for the modernization of Annie Gale School starting in 2026. On September 18, 2024, AE&C announced that design funding was being provided immediately to accelerate the delivery timeline. The project is being managed by CBE and on April 1, 2025, the design contract was awarded with design development currently underway.

On March 1, 2024, the GoA announced that “Planning” funding for a new middle school located in the community of Saddle Ridge would be provided in 2026. On September 26, 2024, AE&C announced that “Planning” funding was being provided immediately to accelerate the delivery timeline. Work for the “Planning” phase is complete and the project is currently awaiting confirmation of site readiness.

On March 14, 2025, the GoA announced approval of “Design” funding for ten new CBE elementary and middle schools located throughout various communities in Calgary. On April 25, 2025, AE&C and AI representatives advised that all ten schools will be bundled and delivered under a single P3 contract. The project start-up meeting was held on July 10, 2025, and design meetings are anticipated to start in the fall.

The MCP provides school jurisdictions with new modular classrooms, modular/portable unit relocations, replacements and demolitions to assist school jurisdictions with the accommodation of students on an urgent basis. On March 14, 2024, as part of the 2024-25 MCP, AE&C approved 12 new modular classrooms and the relocation of six other units. On April 9, 2024, the CBE Board of Trustees approved the use of Capital Reserves to relocate six modular classrooms. On August 2, 2024, as a part of the 2024-25 MCP, AE&C provided in-year approval of an additional 35 new and the relocation of five modular classrooms. The majority of projects are into the warranty phase and will not be included in this report going forward; three sites are in the final stages of construction and will remain in the report. On April 17, 2025, under the 2025-26 MCP, AE&C provided approval for eight new modular classrooms and one demolition. On July 9, 2025, AE&C provided in-year approval for up to 13 additional new modular classrooms. All 2025-26 projects are currently in the design phase.

#### 4 | Analysis

---

Information on the status of the abovementioned projects is provided in **Attachment I**.

The locations of the various new school, existing school and MCP capital projects are shown in **Attachment II**.

**Attachment III** provides a series of onsite photographs to visually convey the progress at Evanston middle.

There are four Project Steering Committees set up for the following projects:

- Evanston elementary;
- Redstone elementary;
- Cornerstone high school; and
- Annie Gale School Modernization

## 5 | Conclusion

---

This report provides the current update on the status of all approved new and existing school capital projects as well as all approved projects under the MCP. It is provided to the Board of Trustees for informational purposes in compliance with Operational Expectation 7: Communication With and Support for the Board.

JOANNE PITMAN  
CHIEF SUPERINTENDENT OF SCHOOLS

### ATTACHMENTS

Attachment I: New/Modernized Facility Construction Status  
Attachment II: Project Location Map  
Attachment III: Construction Photos

### GLOSSARY – Developed by the Board of Trustees

Board: Board of Trustees

Governance Culture: The Board defined its own work and how it will be carried out. These policies clearly state the expectations the Board has for individual and collective behaviour.

Board/Chief Superintendent Relationship: The Board defined in policy how authority is delegated to its only point of connection – the Chief Superintendent – and how the Chief Superintendent's performance will be evaluated.

Operational Expectations: These policies define both the nonnegotiable expectations and the clear boundaries within which the Chief Superintendent and staff must operate. They articulate the actions and decisions the Board would find either absolutely necessary or totally unacceptable.

Results: These are our statements of outcomes for each student in our district. The Results policies become the Chief Superintendent's and the organization's performance targets and form the basis for judging organization and Chief Superintendent's performance.

**CALGARY BOARD OF EDUCATION  
NEW & EXISTING SCHOOL CONSTRUCTION STATUS  
As of August 26, 2025**

Building	Opening Date	Notes/Comments
41. Evanston Heights School Grades 5-9* New School, Capacity 900 students Construction approval	TBD	Design Build – RFP Package (includes drawing package to 30% development and Performance Specifications) 100%
		Design-Build Contract Award 100%
		Design and Specifications 99%
		Construction Progress 65%
		Note: Project managed by Alberta Infrastructure (AI). Design-build contractor mobilized to site in late April 2024. Building envelope complete, mechanical and electrical rough-ins ongoing, interior finishes started.
43. John G. Diefenbaker School Grades 10-12 Replacement, Capacity 1,910 Design approval	TBD	Planning Phase 100%
		Design and Specifications 0% Note: Project managed by AI. Additional 'Planning' activities approved and completed. On July 16, 2025, Alberta Education and Childcare (AE&C) announced approval to change the scope from 'modernization' to 'replacement' and to proceed with design-only. Design expected to start in the fall.
44. Annie Gale School Grades 6-9 Modernization Design approval	TBD	Design and Specifications 15%
		Note: Project being managed by Calgary Board of Education (CBE). Design approval received on September 18, 2024. Prime consultant contract has been awarded. Schematic design is complete; design development is ongoing.
45. Cornerstone High School Grades 10-12* New School, Capacity 2,400 students Construction approval	TBD	Design and Specifications 20%
		Note: Project managed by AI. Design approval was announced on March 1, 2024. Construction approval announced on February 15, 2025. Internal engagement is ongoing. Design development is underway.
48. Saddle Ridge Middle School Grades 5-9* New School, Capacity 900 students Planning approval	TBD	Planning Phase 97%
		Note: Planning approved on March 1, 2024. Planning activities are in the final stages of completion. Project is awaiting confirmation of site readiness prior to requesting start of next phase.
49. Evanston Elementary School Grades K-4* New School, Capacity 600 students Construction approval	TBD	Design and Specifications 25%
		Construction Award 50%
		Construction Progress 0%
		Note: Project managed by AI. Project announced for design and construction on March 1, 2024. Design development is complete. P3 procurement by AI is underway.

\*Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.

**CALGARY BOARD OF EDUCATION  
NEW & EXISTING SCHOOL CONSTRUCTION STATUS  
As of August 26, 2025**

Building	Opening Date	Notes/Comments	
50. Redstone Elementary School Grades K-4* New School, Capacity 890 students Construction approval	TBD	Design and Specifications	25%
		Construction Award	30%
		Construction Progress	0%
		Note: Project managed by AI. Project announced as design-only on March 1, 2024 and approved for construction on February 15, 2025. Design development is complete. P3 procurement by AI is underway.	
51. Aspen Woods Middle School Grades 5-9* New School, Capacity 900 students Design approval	TBD	Design and Specifications	0%
		Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	
52. Cityscape/Redstone Middle School Grades 6-9* New School, Capacity 1,200 students Design approval	TBD	Design and Specifications	0%
		Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	
53. Cornerstone Elementary School Grades K-5* New School, Capacity 900 students Design approval	TBD	Design and Specifications	0%
		Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	
54. Livingstone Elementary School Grades K-5* New School, Capacity 900 students Design approval	TBD	Design and Specifications	0%
		Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	
55. Mahogany Middle School Grades 7-9* New School, Capacity 1,200 students Design approval	TBD	Design and Specifications	0%
		Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	
56. Nolan Hill Elementary School Grades K-4* New School, Capacity 600 students Design approval	TBD	Design and Specifications	0%
		Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	

*\*Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.*

**CALGARY BOARD OF EDUCATION  
NEW & EXISTING SCHOOL CONSTRUCTION STATUS  
As of August 26, 2025**

Building	Opening Date	Notes/Comments				
57. Sage Hill Elementary School Grades K-5* New School, Capacity 600 students Design approval	TBD	<table><tr><td>Design and Specifications</td><td>0%</td></tr><tr><td colspan="2">Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.</td></tr></table>	Design and Specifications	0%	Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	
Design and Specifications	0%					
Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.						
58. Sage Hill/Kincora Middle School Grades 6-9* New School, Capacity 1,000 students Design approval	TBD	<table><tr><td>Design and Specifications</td><td>0%</td></tr><tr><td colspan="2">Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.</td></tr></table>	Design and Specifications	0%	Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	
Design and Specifications	0%					
Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.						
59. Sherwood/Nolan Hill Middle School Grades 5-9* New School, Capacity 900 students Design approval	TBD	<table><tr><td>Design and Specifications</td><td>0%</td></tr><tr><td colspan="2">Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.</td></tr></table>	Design and Specifications	0%	Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	
Design and Specifications	0%					
Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.						
60. Cornerstone Middle School Grades 6-9* New School, Capacity 1,200 students Design approval	TBD	<table><tr><td>Design and Specifications</td><td>0%</td></tr><tr><td colspan="2">Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.</td></tr></table>	Design and Specifications	0%	Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.	
Design and Specifications	0%					
Note: Project managed by AI. Project announced as design-only on March 14, 2025. Internal feedback gathering ongoing. Kick-off meeting held on July 10, 2025. Design expected to start in the fall.						

*\*Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.*

**CALGARY BOARD OF EDUCATION  
MODULAR CLASSROOM PROGRAM STATUS  
As of August 26, 2025**

Building	Number of Units	Type	Opening Date	Notes/Comments	
M7. Connaught School Grades K-6 Added Capacity: 150	4	New	Summer 2025	Design and Specifications	100%
	2	Relocation		Construction Award	100%
				Construction Progress	99%
				Note: Four new modulares approved on March 14, 2024 and two relocated modulares approved on April 9, 2024. Project substantially complete and final inspections scheduled. Work ongoing to address deficiencies.	
M8. Nelson Mandela HS Grades 10-12 Added Capacity: 150	6	New	Summer 2025	Design and Specifications	100%
				Construction Award	100%
				Construction Progress	99%
				Note: Approved on March 14, 2024. Project complete and occupancy granted. Work ongoing to address deficiencies.	
M9. Prairie Sky School Grades K-9 Added Capacity: 175	3+1	New	Summer 2025	Design and Specifications	100%
	4	Relocation		Construction Award	100%
				Construction Progress	90%
				Note: Four relocated modulares approved on April 9, 2024 and three new modular classrooms plus one new modular washroom approved on August 2, 2024. Construction activities underway.	
M10. Peter Lougheed School Grades 5-9 Added Capacity: 100	4	New	Summer 2025	Design and Specifications	100%
				Construction Award	100%
				Construction Progress	99%
				Note: Two new modulares approved on March 31, 2024 and two new modulares approved on August 2, 2024. Project complete and occupancy granted. Work ongoing to address deficiencies.	
M12. Joane Cardinal-Schubert HS Grades 10-12 Added Capacity: 150	5	Relocation	Summer 2025	Design and Specifications	100%
	1	New		Construction Award	100%
				Construction Progress	90%
				Note: Approved on August 2, 2024. Construction activities underway.	
M13. Mahogany School Grades K-5 Added Capacity: 100	4	New	Summer 2025	Design and Specifications	100%
				Construction Award	100%
				Construction Progress	97%
				Note: Approved on August 2, 2024. Project nearing substantial completion and final inspections are being scheduled.	

*\*Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.*

**CALGARY BOARD OF EDUCATION  
MODULAR CLASSROOM PROGRAM STATUS  
As of August 26, 2025**

Building	Number of Units	Type	Opening Date	Notes/Comments	
M14. North Trail HS Grades 10-12 Added Capacity: 150	6	New	Summer 2025	Design and Specifications	100%
				Construction Award	100%
				Construction Progress	97%
				Note: Approved on August 2, 2024. Project nearing substantial completion and final inspections are being scheduled.	
M15. Hugh A. Bennett School Grades K-4 Added Capacity: 100	4	New	Summer 2025	Design and Specifications	100%
				Construction Award	100%
				Construction Progress	90%
				Note: Approved on August 2, 2024. Construction activities underway.	
M16. Grant MacEwan School Grades K-6 Added Capacity: 150	6	New	Summer 2025	Design and Specifications	100%
				Construction Award	100%
				Construction Progress	99%
				Note: Approved on August 2, 2024. Project substantially complete and final inspections scheduled. Work ongoing to address deficiencies.	
M17. Colonel Irvine School Grades 5-9 Added Capacity: 100	4	New	Summer 2025	Design and Specifications	100%
				Construction Award	100%
				Construction Progress	99%
				Note: Approved on August 2, 2024. Project substantially complete and final inspections scheduled. Work ongoing to address deficiencies.	
M18. Buffalo Rubbing Stone School Grades K-5 Added Capacity: 50	2	New	Summer 2025	Design and Specifications	100%
				Construction Award	100%
				Construction Progress	97%
				Note: Approved on August 2, 2024. Project nearing substantial completion and final inspections are being scheduled.	
M19. Kenneth D. Taylor School Grades K-6 Added Capacity: 50	2	New	Summer 2025	Design and Specifications	100%
				Construction Award	100%
				Construction Progress	97%
				Note: Approved on August 2, 2024. Project nearing substantial completion and final inspections are being scheduled.	

*\*Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.*

**CALGARY BOARD OF EDUCATION  
MODULAR CLASSROOM PROGRAM STATUS  
As of August 26, 2025**

Building	Number of Units	Type	Opening Date	Notes/Comments	
M20. John G. Diefenbaker HS Grades 10-12 Added Capacity: 150	6	New	TBD	Design and Specifications	50%
				Construction Award	0%
				Construction Progress	0%
				Note: Approved on April 17, 2025. Design activities ongoing.	
M21. Dr. E.P. Scarlett HS Grades 10-12 Added Capacity: 150	6	New	TBD	Design and Specifications	50%
				Construction Award	0%
				Construction Progress	0%
				Note: Approved on July 9, 2025. Design activities ongoing.	
M22. Mount Royal School Grades 7-9 Added Capacity: 75	3	New	TBD	Design and Specifications	85%
				Construction Award	0%
				Construction Progress	0%
				Note: Two units approved on April 17, 2025, and four units approved on July 9, 2025. Design activities ongoing.	
M23. Centennial HS Grades 10-12 Added Capacity: 150	6	New	TBD	Design and Specifications	95%
				Construction Award	0%
				Construction Progress	0%
				Note: Approved on July 9, 2025. Design activities are almost complete.	

*\*Grade configurations reflect those approved through the Three-Year School Capital Plan. Actual opening day grade configurations will be confirmed prior to school opening.*

# New and Modernized Schools As of September 2025








Attachment II


## Existing Schools

- #43 John G. Diefenbaker HS replacement
- #44 Annie Gale MS modernization

## New Schools

- #41 Evanston Heights
- #45 Cornerstone HS
- #48 Saddle Ridge MS
- #49 Evanston ES
- #50 Redstone ES
- #51 Aspen Woods MS
- #52 Cityscape/Redstone ES
- #53 Cornerstone ES
- #54 Livingston ES
- #55 Mahogany MS
- #56 Nolan Hill ES
- #57 Sage Hill ES
- #58 Sage Hill/Kincora MS
- #59 Sherwood/Nolan Hill MS
- #60 Cornerstone MS


-  New Schools
-  Modernized Schools
-  CBE Boundary
-  City Boundary
-  Community Boundary
-  Greenspace
-  Water Body

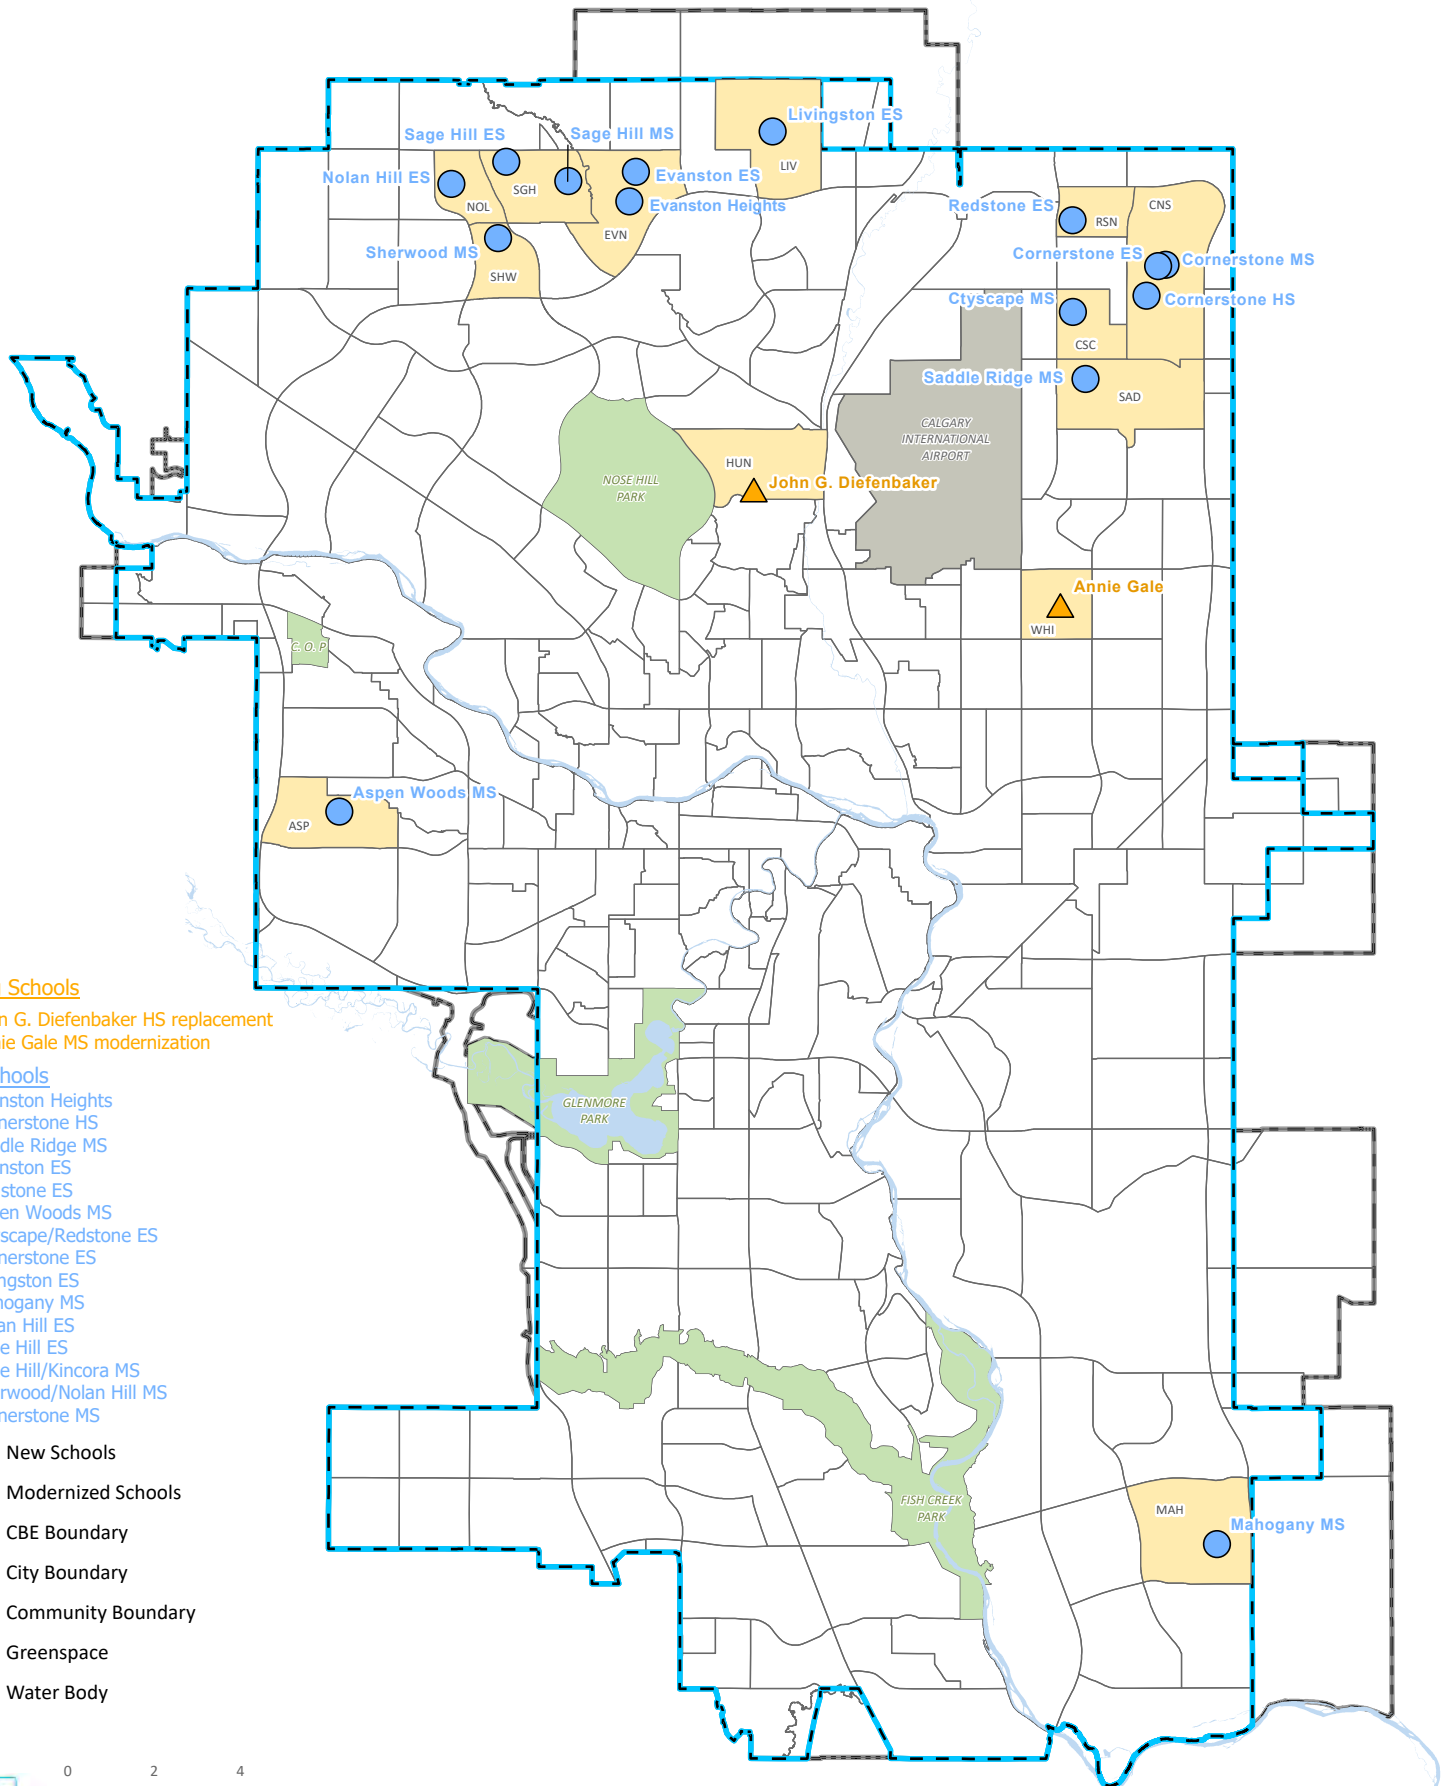

# Modular Classroom Program

Attachment II

As of September 2025

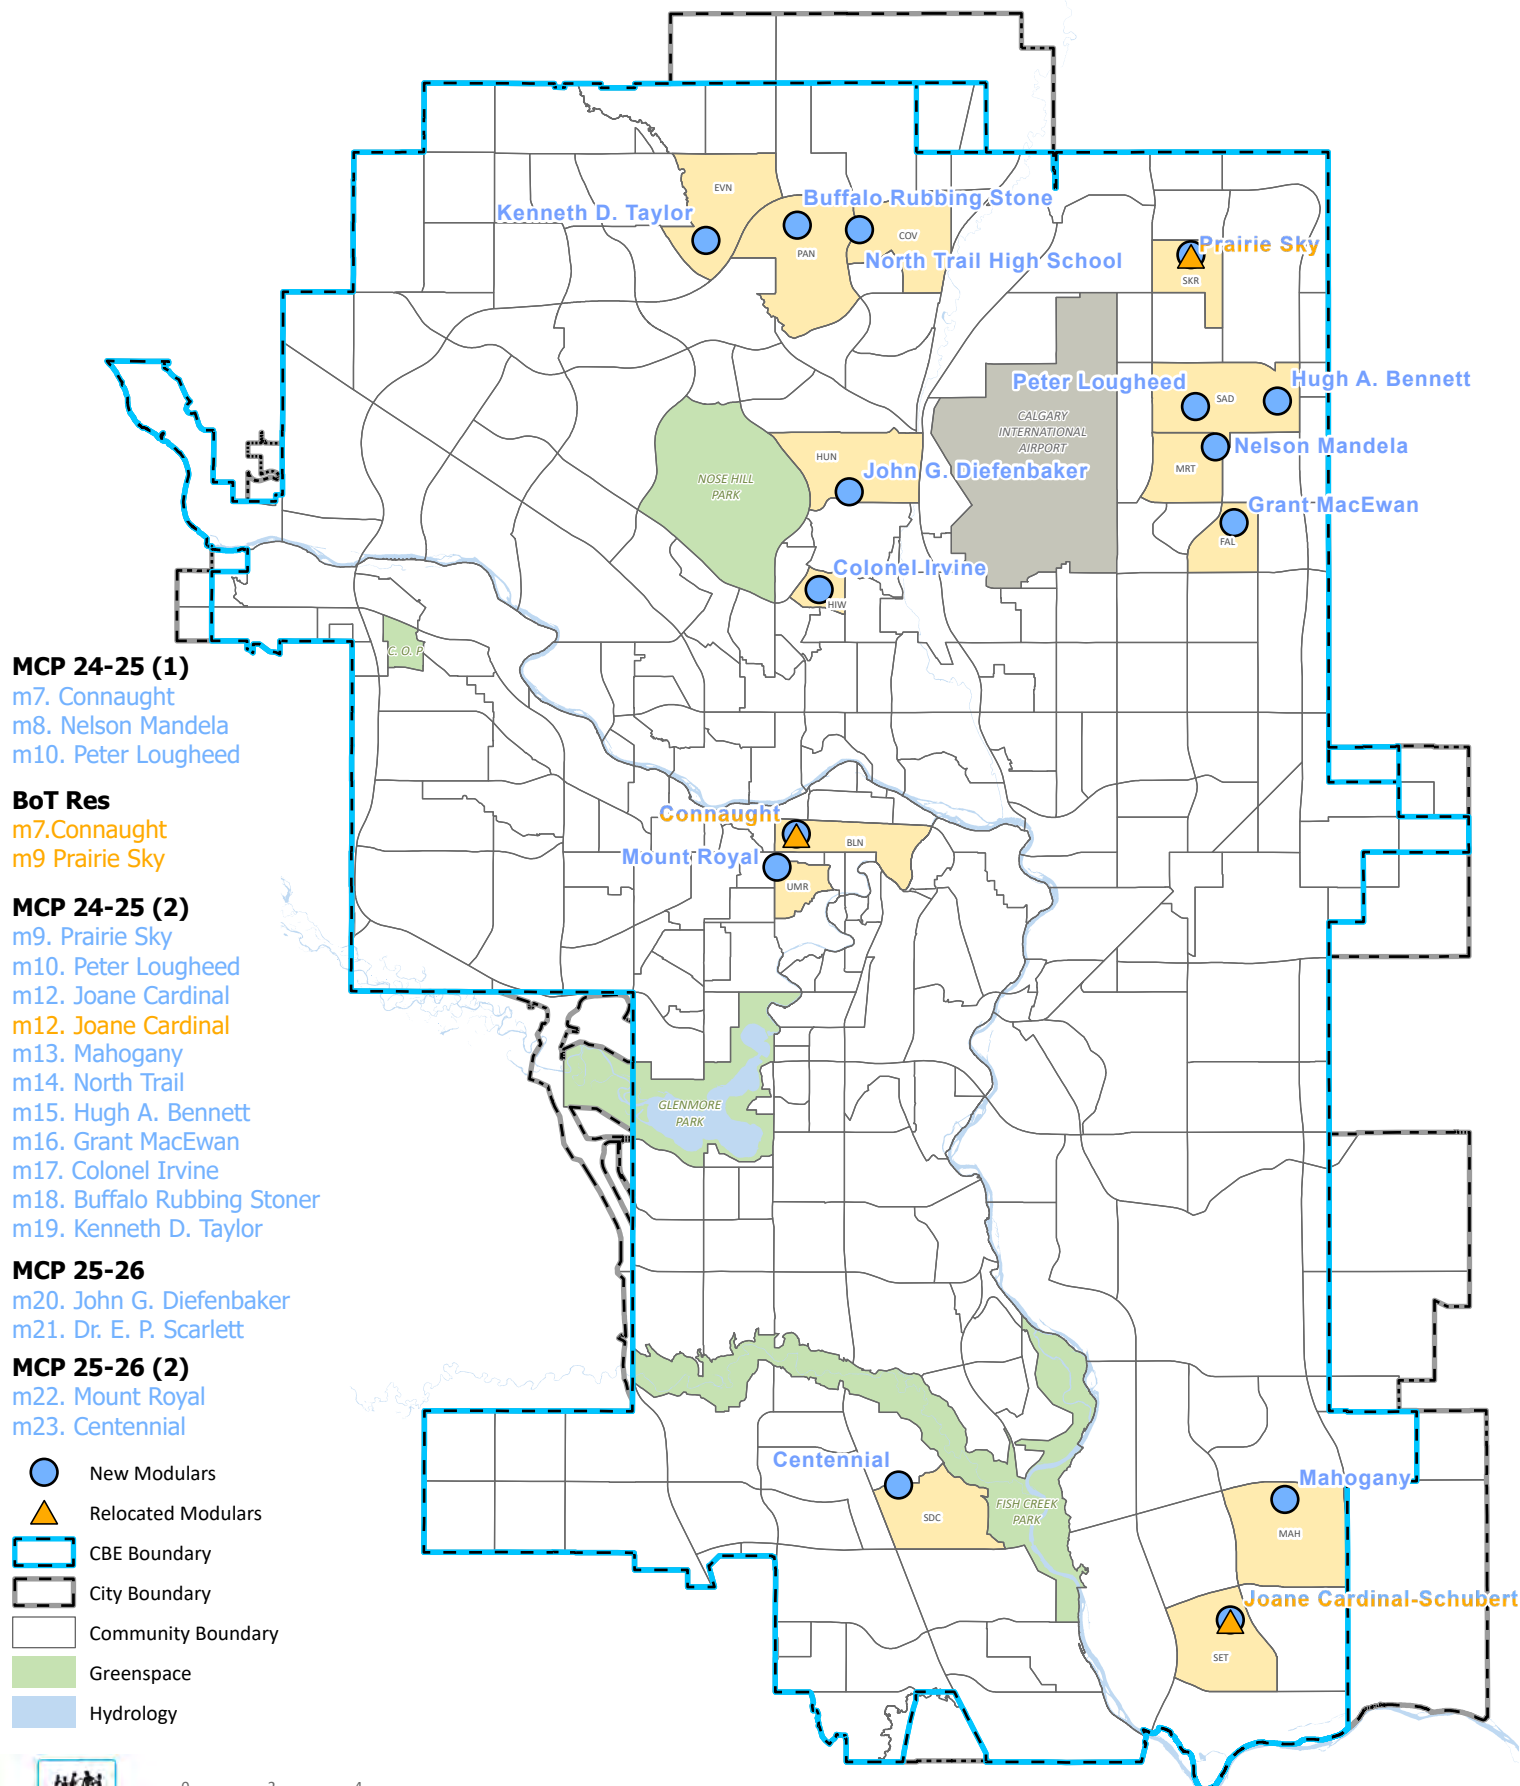

Calgary Board  
of Education

0 2 4 km

1:175,000  
NAD 1983 3TM 114  
Date: August 26, 2025  
Prepared by: Planning  
Map: Modular Program



## Evanston Heights School



Interior



Interior



Exterior



Exterior
